EXCEL Environmental Resources, Inc.

INDEPENDENT COMMUNITY MONITORING

REPORT No. 6

Monitoring Period: Monday, May 5th, 2025 through Friday, June 13th, 2025

1.0 Project Background and Role of the Independent Community Monitor (ICM):

Excel Environmental Resources, Inc. (Excel) has been contracted by the New York City Department of Design and Construction (NYCDDC) to serve as the ICM for the Borough Based Jails Program – Manhattan Dismantle and Swing Space (BBJ-MDSS) project for independent oversight of the dismantling project given the proximity of adjacent sensitive receptors, including residents, commercial/retail businesses and institutions, the courthouse, and parks. ***Following the text of this ICM Report No. 6 is a Data Summary Report which is 19 pages in length.***

On behalf of the NYCDDC, the joint venture of AECOM and Hill International (AECOM-Hill JV) is the construction manager for the BBJ-MDSS project and the Gramercy Group, Inc. (Gramercy) is the demolition, or dismantling, contractor. In addition, geotechnical soil borings, monitoring wells, and test pits were installed on behalf of the design/build contractor with onsite oversight of the drilling being conducted by Langan with AECOM-Hill reporting that this work completed on or before May 30, 2025. The work also includes excavation of test pits and performance of soil borings for collection of soil samples for laboratory analysis in preparation for the future work at the Site.

During the reporting period, site activities were conducted from 7 AM to 3:30 PM Monday through Friday, weather permitting. Dust, noise, and vibration monitoring is conducted by Vibranalysis, Inc. on behalf of Gramercy on a 24-hour per day basis. In addition, during the geotechnical investigation, Langan operated one upwind and one downwind CAMP air quality monitoring station located in the northeast corner of the Site inside the fence line which was removed prior to Excel's June 10th, 2025 site visit as further discussed in Section 3.0 of this report.

As ICM, Excel provides the following ICM services on behalf of the community:

- Daily review of the dust, noise, and vibration monitoring data for completeness and compliance with established threshold and alert action levels. During the reporting period, air quality and noise monitoring was conducted 24 hours per day at six Community Air Monitoring Plan (CAMP) located around the perimeter and off the Site, designated **AQS-001, AQS-975, AQS-977, AQS-993, AQS-997, and AQS-998** as shown in the Site Map provided as Page 2 of 19 of the enclosed Data Summary Report.
- In addition, there were 14 perimeter vibration monitoring stations designated **R04, R05, R06, R07, R08, R09, R10, R11, R12, R13, R14, R16, R16, and R17** as also shown in the Site Plan provided as Page 2 of 19 of the enclosed Data Summary Report until May 30th, 2025 when Gramercy removed the vibration monitors R04, R05, R06, R07 from the Chung Pak Building because the dismantling associated with the building and the geotechnical investigation activities had all been completed.

- **Dust Threshold Level**: 100 micrograms per cubic meter (100 ug/m^3) for airborne particulate matter less than 10 micrometers in size (PM-10) based on a 15-minute time weighted average (TWA). If exceeded, onsite activities are adjusted if necessary, and additional dust suppression measures must be used.
- **Dust Alert/Stop Work Level**: 150 ug/m^3 for PM-10 based on a 15-minute TWA which is considered the Short-Term Exposure Limit (STEL). The Permissible Exposure Limit (PEL), the regulatory limit to protect public health and welfare with respect to PM-10, is based on a 24-hour TWA. The 15-minute TWA, or STEL, is used to aid the BBJ-MDSS Project Team to monitor the project's effect on PM-10 air quality more closely. If the 15-minute TWA for PM-10 is exceeded, work is stopped, the source (s) are evaluated, onsite activities are adjusted if/as necessary, additional best management practices (BMPs) implemented prior to resuming work, and dust levels confirmed to be below threshold and alert levels.
- **Noise Alert Level:** Weekdays between 7 AM and 6 PM, noise from Site activities cannot exceed 80 A-weighted decibels (dBA) measured 50 or more feet from the property line, or 70 dBA or an increase of 7 dBA above ambient background, whichever is higher, on weekday evenings between 6 PM and 7 AM and all day/night on weekends.
- **Vibration Warning and Action Levels:** A warning level of 0.5 inches per second (in/sec) at which point onsite activities are evaluated to determine if any adjustments need to be made and work must be stopped and the work area inspected if vibrations at one or more monitoring stations are measured above the action level of 1.0 in/sec.

- Follow up with the AECOM-Hill JV and NYCDDC project representatives to discuss any exceedance or excursion of one or more alert action level, evaluate the findings of their investigation of the cause (s) and corrective action (s) taken to mitigate the situation and restore the alert condition to below threshold levels.

  - Excel receives daily excursion investigation summaries for review to evaluate the cause of any noise, dust, or vibration alert level exceedance, the scope of investigation, and the corrective actions taken if related to onsite activities.

- Conduct one monthly unscheduled Site inspection to include real-time verification of dust and noise levels at and surrounding the Site and observe and photo-document the ongoing dismantling activities for adherence to monitoring plans and BMPs.
- Prepare and submit ICM reports summarizing the results of the dust, noise, and vibration monitoring noting any exceedance of the alert action levels, relaying the cause (s) of the exceedance as determined by the NYCDDC project team based on investigation of each alert, the corrective action (s) taken in response to the exceedance, Excel's findings and observations during our once per month Site inspection, and outlining additional recommendations, if any.
- Participation in the Working Group, or similar meetings, with the NYCDDC project team, representatives of the community and local elected officials and other stakeholders to discuss Excel's findings and observations related to Site activities and dust, noise, and vibration monitoring data, relay any issue of concern and associated recommendation (s) to address or mitigate the concern, and answer questions from the participants at the meeting.
- Respond to questions or concerns raised by the community and/or elected officials if not appropriately and timely addressed by the NYCDDC project team and provide Excel's observations and any recommendations via email or conference call as the dismantling activities progress.

2.0 Dismantling and Other Onsite Activities During the Reporting Period May 5th, 2025 through June 13th, 2025

- North Courthouse 3rd and 12th Floor Bridge Infill and brickwork;
- Continuation of the geotechnical investigation activities during the first half of the reporting period including:

    - Grading and redistribution of crushed concrete to facilitate drill rig access to drilling locations
    - Drilling of geotechnical soil borings, installation of monitoring wells and associated groundwater sampling, and test pit activities.
    - As noted in Section 3.0 of this report, the geotechnical investigation was completed on or about Friday, May 30th, 2025.

- Noise, dust, and vibration monitoring continued 24-hours/day although as noted in Section 4.0, the remaining four vibration monitors located in the Chung Pak building, R04 through R07, were removed on or about May 30th, 2025 following completion of the geotechnical investigation.
- Implementation of dust mitigation BMPs, weather permitting and if/as needed for controlling dust generation on Site as necessary to ensure that dust levels at the offsite monitoring stations are maintained below alert levels
- Implementation of noise mitigation BMPs, including use of sound attenuation blankets and movable acoustic barriers placed around active dismantling operations, onsite monitoring of noise during movement of equipment and adjusting heavy machinery as necessary to reduce bounce back from adjacent structures, etc.

3.0 Excel's Site Visits Work Scope, Findings, and Observations:

Excel's Site Visits Work Scope, Findings, and Observations:

A. June 10th, 2025 Site Visit

- Ms. Megan DeMatteo of Excel conducted an unscheduled visit to the Site on June 10th, 2025 to verify offsite and onsite noise and dust/particulate levels arriving at the Site at 9:00 AM. Weather conditions were rain with the temperature between 60- and 68-degrees Fahrenheit.

- Using a hand-held PDR-100 Multi-Ram Dust Monitor and an Edge 5 Noise Dosimeter, M. DeMatteo of Excel took real time, instantaneous dust/particulate and noise readings at the five (5) of the offsite, outside perimeter CAMP monitoring stations surrounding the Site with the results summarized as follows:

    - **Offsite CAMP Station AQS 975**: Dust/particulates and noise measured below action levels at 5.0 ug/m^3 and 66.4 dBA, respectively.
    - **Offsite CAMP Station AQS 977:** Dust/particulates and noise measured below action levels at 2.0 ug/m^3 and 63.6 dBA, respectively.
    - **Offsite CAMP Station AQS 993**: Dust/particulates and noise measured below action levels at 4.0 ug/m^3 and 62.4 dBA, respectively.

- **Offsite CAMP Station AQS 997:** Dust/particulates and noise measured below action levels at 2.0 ug/m^3 and 66.8 dBA, respectively.
- **Offsite CAMP Station AQS 998:** There was no measurable dust/particulates and noise was measured below the action level at 67.6 dBA.

➢ M. DeMatteo visually inspects the sidewalk and roadway opposite the Site entrance/exit for any visible sign of dust/particulate tracking offsite. Although it had been raining and the sidewalk and pavement was visibly wet with some puddled water, there was some visible soil/crushed concrete on the sidewalk in the immediate vicinity of the gate as shown in Photo No. 1 provided in Data Summary Report No. 6, however, there was no visible indication of tracking into the roadway. (**See Photos No. 1 through 4 of the Data Summary Report No. 6**).

➢ M. DeMatteo proceeds to the construction Site with M. Schnurr of AECOM-Hill to gain onsite access and observe current Site activities while taking real-time, instantaneous dust/particulate and noise readings on the Site using the hand-held PDR-100 Multi-Ram Dust Monitor and Edge 5 Noise Dosimeter, respectively.

- M. Schnurr escorts M. DeMatteo across the Site and she photographs the Site conditions and ongoing activities which include in-fill and brick work in progress on the Courthouse (**See the Site Photographs in the enclosed Data Summary Report No. 6).**

- M. Schnurr stated that the geotechnical investigation was completed on or about Friday, May 30th, 2025 which was presumably when Langan also removed the upwind and downwind onsite CAMP stations they had been using for air quality monitoring.

- Onsite, real-time, instantaneous dust/particulate levels were measured using the hand-held PDR-100 Multi-Ram Dust Monitor and noise was measured using a hand-held Edge 5 Noise Dosimeter with measurements summarized as follows:

  - Dust/particulate levels were below the action level with measurements ranging from none measurable to 19.0 ug/m3.
  - Noise levels were below the action level with measurements ranging from 63.3 to 71.5 dBA.

- M. Schnurr accompanies M. DeMatteo to the offsite, perimeter CAMP Stations which are all in operation and M. DeMatteo collects instantaneous, real-time dust and noise measurements using the hand-held PDR-100 Multi-Ram Dust Monitor and an Edge 5 Noise Dosimeter, respectively. The readings are as follows:

  - **Offsite CAMP Station AQS 975:** No measurable dust/particulates and noise measured below the action level at 63.7 dBA.
  - **Offsite CAMP Station AQS 977:** No measurable dust/particulates and noise measured below the action level at 63.1 dBA.
  - **Offsite CAMP Station AQS 993:** No measurable dust/particulates and noise measured below the action level at 64.1 dBA.
  - **Offsite CAMP Station AQS 997:** No measurable dust/particulates and noise measured below the action level at 63.2 dBA.

- **Offsite CAMP Station AQS 998:** No measurable dust/particulates and noise measured below the action level at 67.4 dBA.

- M. Schnurr then accompanies M. DeMatteo to the AECOM-Hill construction office for her to sign in.

- M. DeMatteo completed the Site visit at 11:00 AM.

4.0 Summary of Daily Dust Monitoring Data: During the monitoring period, air quality monitoring was conducted 24 hours per day at six (6) air quality CAMP stations located around the perimeter designated **AQS-001, AQS-975, AQS-977, AQS-993, AQS-997,** and **AQS-998**. The CAMP monitoring station locations are shown on the Site Plan provided as Page 2 of 19 of the enclosed Data Summary Report No. 6.

Daily Dust Monitoring data graphs are provided in Section 1, Pages 3 through 6 of 19 of the enclosed Data Summary Report No. 6. Breaks in monitoring data on the graphs generally indicate loss of battery, battery replacement, and equipment maintenance periods.

As shown in the Daily Dust Monitoring graphs, there was no exceedance of the Threshold (100 ug/m3) or Alert (150 ug/m3) Dust Levels during the reporting period with dust measurements all extremely low.

As previously stated in Section 1.0 of this report, Langan was also operating one upwind and one downwind CAMP station for monitoring PM-10 dust/particulates and volatile organic compounds (VOCs). Note that, per the project EMP dated January 26, 2022, when VOC monitoring is called for (which in the case of subsurface drilling it would be), the CAMP action level is no more than 5.0 parts per million (ppm) of total VOCs in the ambient air in the vicinity of the work. Langan completed the geotechnical investigation activities on or about Friday, May 30th, 2025. During this time Langan reported to AECOM-Hill that there have been no exceedances of the dust or VOC CAMP action levels.

5.0 Summary of Daily Noise Monitoring Data, May 5th, 2025, through June 13th, 2025

During the monitoring period, noise monitoring was conducted 24 hours per day at six (6) air quality CAMP stations located around the perimeter and off the Site. The CAMP monitoring station locations are shown on the Site Plan provided as Page 2 of 19 of the enclosed Data Summary Report No. 6.

The Daily Noise Monitoring data graphs are also provided in Section 2 on Pages 6 through 9 of 19 of the enclosed Data Summary Report No. 6. Prior to discussing our key observations, we wanted to clarify that there are two readings being taken with respect to noise monitoring. Review of the noise monitoring graphs provided in Section 2, Pages 6 through 9 of the enclosed Data Summary Report No. 6 shows a blue line which represents the "Lmax 1min" which is the highest sound level measured during a one-minute period and a black line which represents the "Leq 20 min" which represents the continuous sound level averaged over a 20-minute period. The Lmax captures the peak noise level within a short time frame, while Leq provides the average noise level over the longer 20-minute duration, including not only sudden loud noises but also quieter times in between.

On Page 3 of the project Environmental Management Plan (EMP) dated January 26, 2022 it states that "the noise level standards/criteria are based on the maximum noise level (Lmax)" and, as previously discussed on Page 2 of this ICM Monitoring Report, the Lmax cannot exceed the 80 dBA alert level as measured 50 or more feet from the source or sources at a point outside the property line or on a

public right-of-way. **For this reason, the Daily Noise Monitoring data graphs provided on Pages 6 through 9 shows both the Lmax (blue line) and Leq (black line) readings.**

Note that breaks in monitoring data on the graphs indicate loss of battery and maintenance periods. Review of the Daily Noise Monitoring data graphs for the reporting period indicates the following:

- **AQS-001 (Court House)** - As shown in the noise monitoring graph on Page 6 of 19 of the Data Summary Report, there were multiple Lmax- 1min (blue line) and Leq- 20 min (black line) exceedances of the 80 dBA alert level spread out over the reporting period.
    - Review of the daily equipment status and excursion reports prepared and provided to Excel by Gramercy indicates that the exceedances were caused by courthouse activities and were not related to the dismantling, or heavy equipment operation at the Site.
- **AQS-977 (Northwest on Centre St.) -** As shown in the noise monitoring graph on Page 7 of 19 of the Data Summary Report No. 6, there were multiple Lmax- 1min (blue line) and significantly fewer Leq- 20 min (black line) exceedances of the 80 dBA alert level spread out over the reporting period.
    - Review of the daily equipment status and excursion reports prepared by Gramercy indicates that the noise exceedances are not related to onsite activities.
- **AQS-993 (Southeast on Baxter St.)** - As shown in the noise monitoring graph on Page 7 of 19 of the Data Summary Report No. 6, there were multiple Lmax- 1min (blue line) and significantly fewer Leq- 20 min (black line) exceedances of the 80 dBA alert level spread out over the reporting period.
    - Review of the daily equipment status and excursion reports prepared by Gramercy and provided to Excel indicates that the noise exceedances were caused by traffic on Baxter Street and are not related to onsite activities.
- **AQS-997 (Northeast on Baxter St.)** - As shown in the noise monitoring graph on Page 8 of 19 of the Data Summary Report No. 6, there were multiple Lmax- 1min (blue line) with significantly fewer Leq- 20 min (black line) exceedances of the 80 dBA alert level spread out over the reporting period.
    - Review of the daily equipment status and excursion reports prepared by Gramercy and provided to Excel indicates that all the exceedances were caused by traffic on Baxter Street are not related to onsite activities.
- **AQS-998 (Baxter St. between White and Walker)** - As shown in the noise monitoring graph on Page 8 of 19 of the Data Summary Report No. 6, there were multiple Lmax- 1min (blue line) with significantly fewer Leq- 20 min (black line) exceedances of the 80 dBA alert level spread out over the reporting period, however, review of the daily equipment status and excursion reports prepared by Gramercy and provided to Excel indicate:
    - Review of the daily equipment status and excursion reports prepared by Gramercy indicates that the noise exceedances are not related to onsite activities.

6.0 Summary of Daily Vibration Monitoring Data, May 5th, 2025 through June 13th, 2025: During this reporting period, vibration monitoring was conducted 24 hours per day at 14 Vibration Monitoring Stations located around the perimeter and off the Site designated **R04, R05, R06, R07, R08, R09, R10, R11, R12, R13, R14, R16, R16, and R17** as shown in the Site Plan provided as Page 2 of 18 of the enclosed Data Summary Report No. 6.

The Daily Vibration Monitoring data graphs are provided in Section 3, Pages 9 through 19 of the enclosed Data Summary Report.

- Review of the data indicates there were the following exceedances of the 1.0 in/sec Maximum Vibration Level, or Stop Work Limit, as follows:

    - As shown on the Site Plan provided on Page 2 of 19 of the enclosed Data Summary Report No. 6, Vibration Monitors R-11, R-14, and R-17 are in the Court House Building. Review of the vibration graphs provided on Page 12 of 19 and Page 15 of 19, respectively, of Data Summary Report No. 6 shows that the following vibration exceedances were recorded during the reporting period:

        - There were two vibration exceedances recorded at Monitor R-11 on Sunday, May 25th, 2025 and Sunday, June 1st, 2025 when there was no work being conducted at the Site therefore this noise level exceedance is related to courthouse activity and/or traffic.
        - There was one vibration exceedance recorded at Monitor R-17 on Tuesday, May 13th, 2025, and one on Thursday, June 3rd, 2025.

            - In their Daily Report, Gramercy indicated the exceedance reported on May 13th, 2025, was not related to onsite activity.
            - Gramercy has also indicated that the noise level exceedance reported on June 3rd, 2025 was related to courthouse activity and/or traffic.

7.0 ICM Overall Findings:

- Review of the ongoing CAMP and vibration monitoring programs and the noise, dust, and vibration monitoring data indicates that the onsite dismantling, heavy equipment operation, and geotechnical investigation practices are being conducted in a manner that is consistent with the agency approved work plans and work scopes.

    - Note, however that, as previously stated in Section 5.0 of this report, on Page 3 of the project Environmental Management Plan (EMP) dated January 26, 2022 for this project, it states that "the noise level standards/criteria are based on the maximum noise level (Lmax)" which cannot exceed the 80 dBA alert level as measured 50 or more feet from the source or sources at a point outside the property line or on a public right-of-way.
    - For this reason, the Daily Noise Monitoring data graphs provided on Pages 6 through 8 of the enclosed Data Summary Report include both the Lmax (blue line) and Leq (black line) readings superimposed on the same graph for ease in comparison.
    - Following Excel's recommendation in our ICM Monitoring Report No. 2, the recent AECOM-Hill Monthly Reports include the Lmax and Leq noise data shown as separate graphs so the

community can compare the noise level data but these reports state that the noise action level is based on the Leq and not the Lmax despite the January 26, 2022 EMP referenced above.

- There were no exceedances of the dust or vibration action levels attributable to onsite dismantling, heavy equipment operation, and/or geotechnical investigation activities.

- As detailed in Section 5.0 of this report, Gramercy has reported that all the elevated noise levels were attributable to traffic and/or activities at the adjacent Courthouse.

- During the Site visit conducted by Excel on June 10th, 2025, M. DeMatteo of Excel verified that all the perimeter, offsite CAMP stations were properly operating and, using hand-held dust/particulate and noise monitors, she verified twice during the inspection that the real-time, instantaneous dust/particulate and noise levels were below action levels at the CAMP locations.

    - M. DeMatteo also used hand-held dust/particulate and noise meters to take instantaneous, real-time onsite dust/particulate and noise measurements in the vicinity of the various ongoing work activities and verified that dust/particulate and noise levels were below the action levels.

- As discussed in Section 8.0 below, with the geotechnical investigation activities completed on or about May 30, 2025, the bulk of the dismantling activities completed with only infill and brick work remaining to be completed, discussions should be ongoing with respect to the CAMP scope, means, and methods prior to initiation of the next phase of construction at the Site.

8.0 ICM Recommendations:

Excel has the following ICM recommendations for the NYCDDC and AECOM-Hill JV project team, which have been previously provided but are reiterated herein as follows:

- Ensure frequent inspection and routine maintenance, as needed, of the onsite truck/equipment tracking pad to ensure that crushed concrete/soil is not tracked off the Site onto the adjacent sidewalk or roadways.

- Currently, dust and noise monitoring is occurring at the remaining six (6) perimeter, offsite CAMP stations shown in the Site Map provided on Page 2 of the enclosed Data Summary Report No. 6 and work is winding down but there is still onsite activity and no instantaneous, real-time monitoring using handheld particulate/dust or noise meters within the various onsite work zones where dust/particulates could become airborne, including very fine PM-2.5 particulates, and noise can be generated.

- As previously recommended in our November 26th, 2024 Weekly Report No. 1, going forward, we recommend that Gramercy conduct daily instantaneous, real time monitoring of PM-10 dust/particulates using a hand held instrument calibrated daily before the start of work and a hand-held noise meter to verify the noise level in the immediate onsite work area to confirm that noise levels recorded at the perimeter CAMP stations are in no way related to onsite activities.

- Additional discussion is also recommended regarding adding PM-2.5 particulate monitoring to supplement the PM-10 particulate monitoring data in the CAMP work scope to ensure the safety and protection of the residents and community.

EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

PROJECT No.:	24846			
PROJECT:	NYC Borough Based Jails System - Manhattan Dismantle and Swing Space	**CLIENT:** New York City Department of Design and Construction (NYDDC)	**DATE:**	Friday, June 27th, 2025
LOCATION:	125 White Street, New York, NY 10013		**MONITOR:**	Excel Environmental Resources, Inc.
		PRESENT AT SITE DURING EXCEL'S June 10th, 2025 SITE VISIT: **Excel** – Megan DeMatteo, Project Scientist/ICM **AECOM-Hill JV** - Michael Schnurr		

COMMUNITY MONITORING WEEKLY STATUS UPDATE: MONDAY, MAY 5th, 2025 - FRIDAY, JUNE 13th, 2025

This Report contains the following:

- A Site Plan showing current CAMP and Vibration Monitoring Station Locations

- Section 1: Community Air Monitoring Weekly Data Summary Dust Monitoring Graphs

- Section 2: Community Air Monitoring Weekly Data Summary Noise Monitoring Graphs

- Section 3: Community Vibration Monitoring Weekly Data Summary Graphs

- Section 4: Photographic Summary


Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.

EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

SITE PLAN WITH MONITORING LOCATIONS:

Environmental Monitoring Manhattan

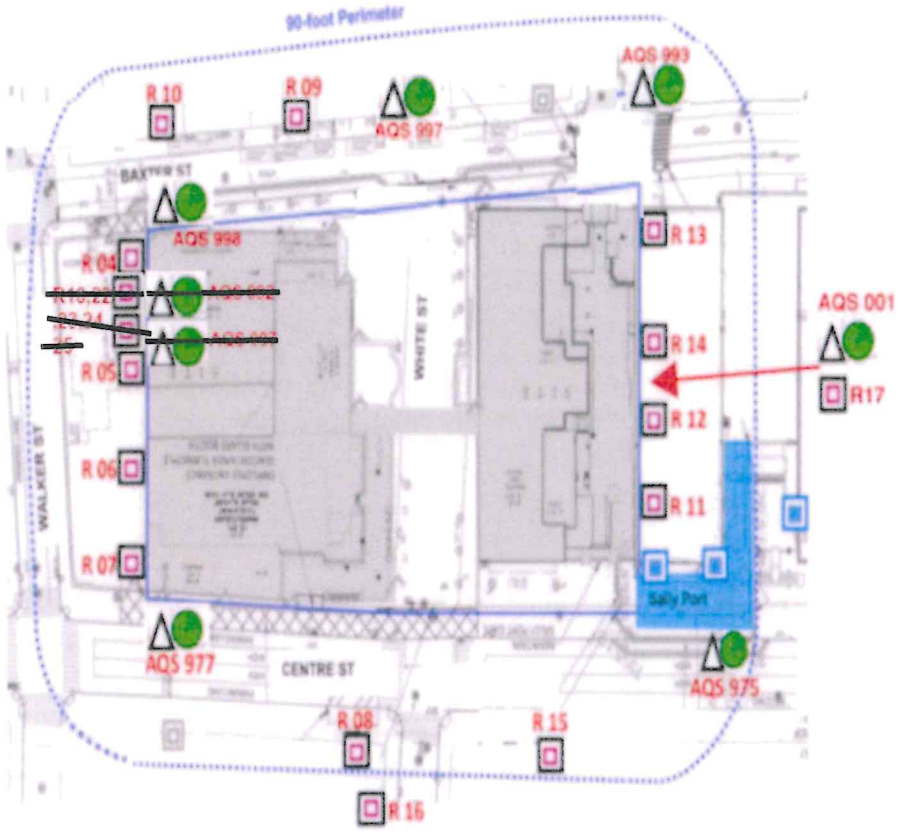

N

* Dismantle project vibration, air and noise monitoring devices are installed by Design-Build team in Phase 2, after sally port construction. A vibration monitoring station was installed in the DCTV Fire house at 87 Lafayette St.

* The location of monitoring stations presented is referential. Air/Noise Monitoring station located in Sally Port area will be relocated in Phase 2.


- Vibration Monitoring Dismantle
- Air Monitoring Station Dismantle
- Noise Monitoring Station Dismantle
- **Vibration Monitoring Sallyport construction (Installed)**
- Vibration Monitoring Not installed

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.


EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

1. Community Air Monitoring Weekly Data Summary: Dust Monitoring (PM10) - 5/5/25 to 6/13/25

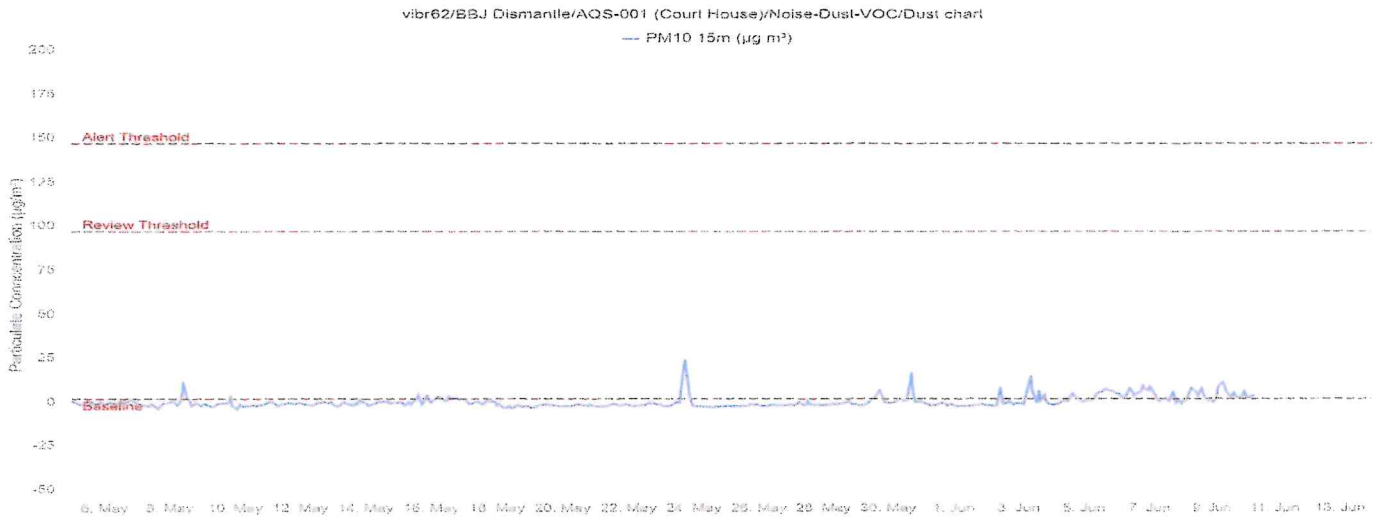

AQS-001 Court House Dust Monitor - 5/5/25 to 6/13/25

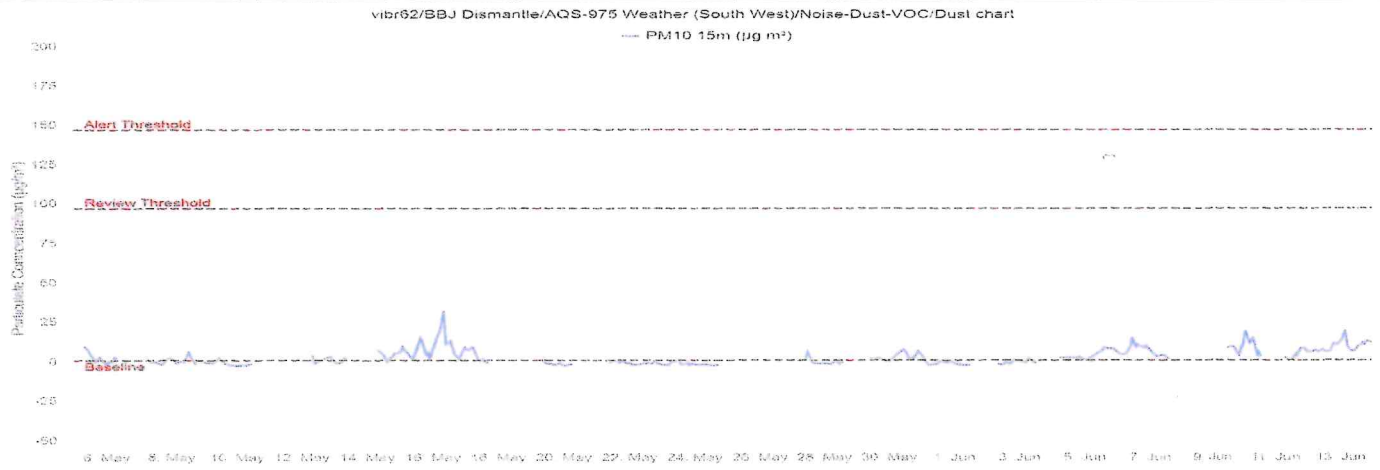


AQS-975 Weather (South West) Dust Monitor - 5/5/25 to 6/13/25

Cc:	Lawra Dodge, Megan DeMatteo, Tim Novy	By:	Brian Ehalt
			Excel Environmental Resources, Inc.


EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

1. Community Air Monitoring Weekly Data Summary: Dust Monitoring (PM10) - 5/5/25 to 6/13/25

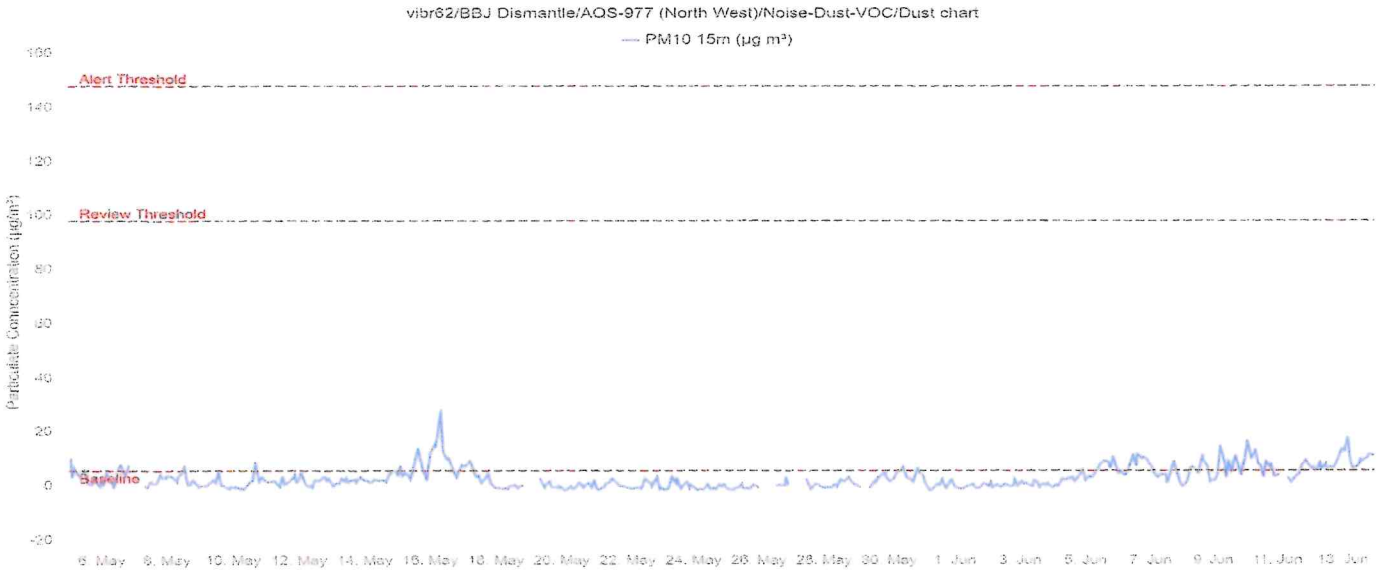

AQS-977 (North West) Dust Monitor - 5/5/25 to 6/13/25

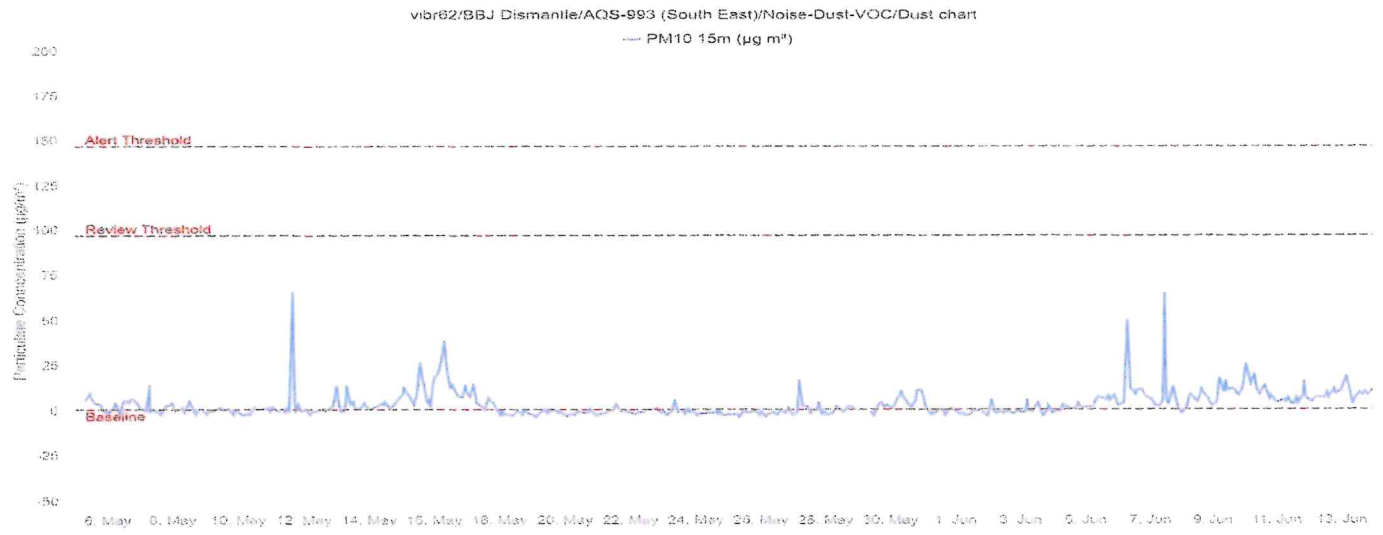


AQS-993 125 Walker Street (South East) Dust Monitor - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.


EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

1. Community Air Monitoring Weekly Data Summary: Dust Monitoring (PM10) - 5/5/25 to 6/13/25

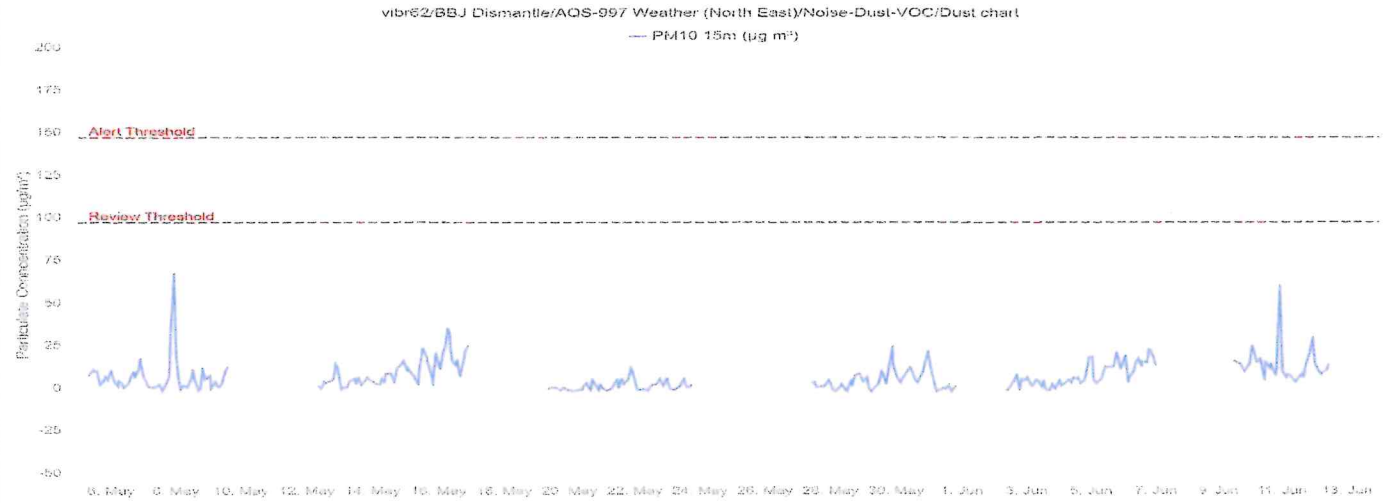

AQS-997 Weather (North East) Dust Monitor - 5/5/25 to 6/13/25

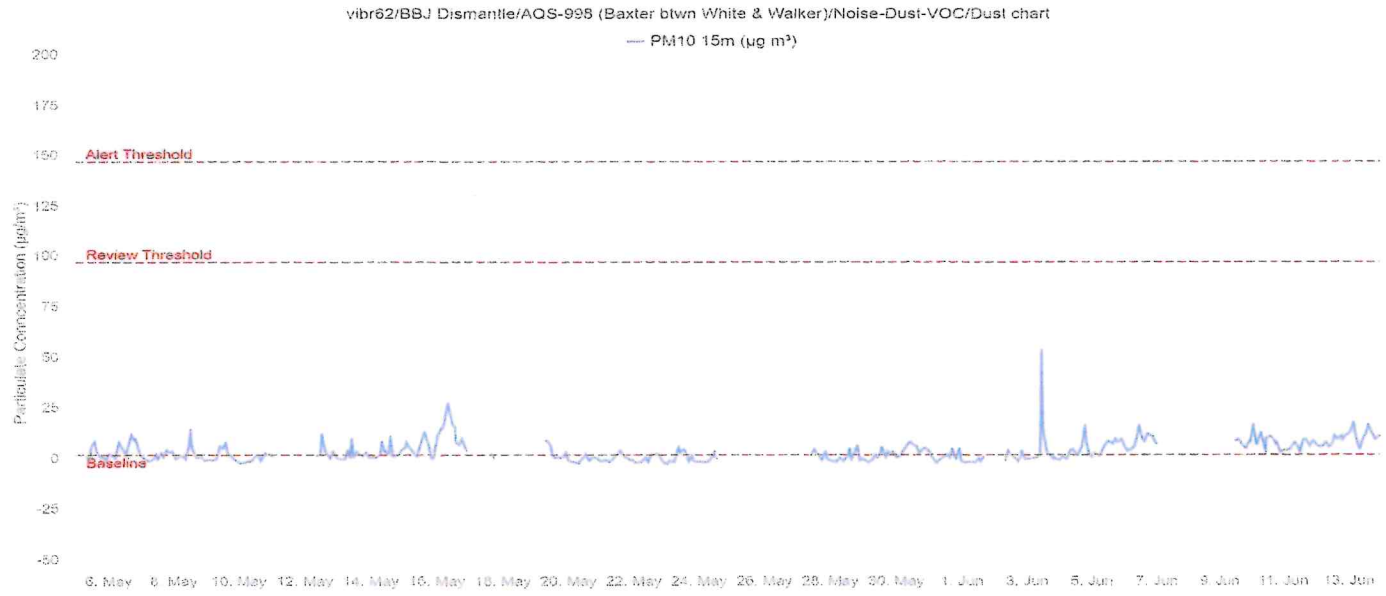


AQS-998 Baxter between White and Walker Dust Monitor - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.


EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

2. Community Air Monitoring Weekly Data Summary: Noise Monitoring - 5/5/25 to 6/13/25

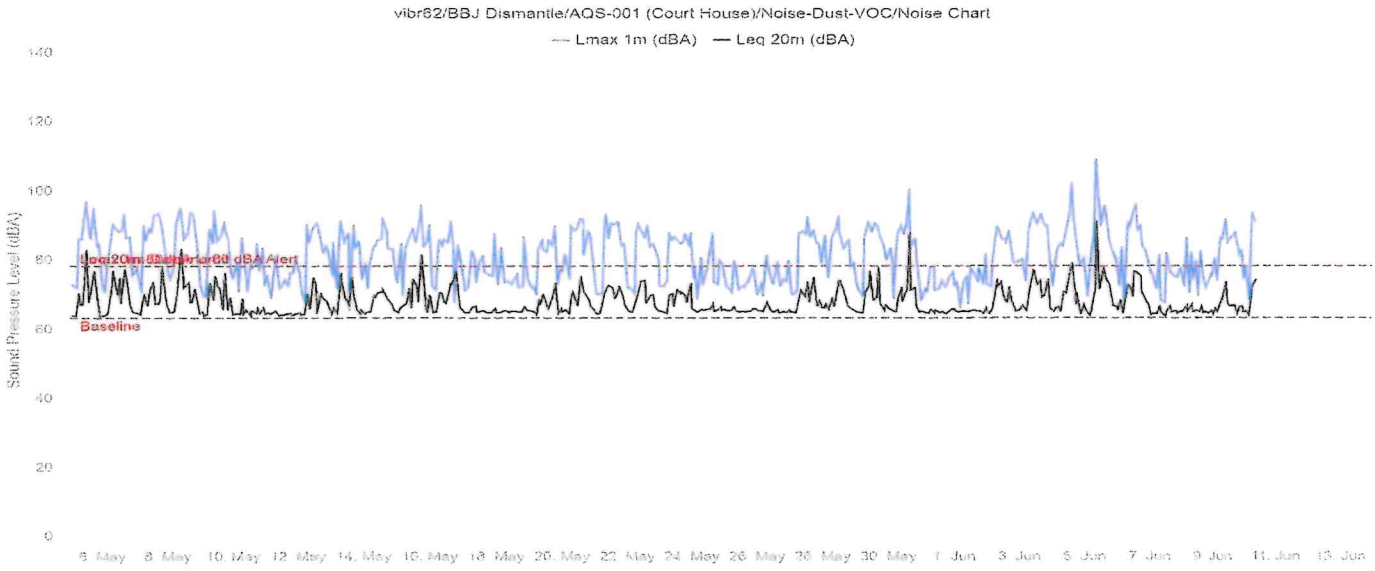

AQS-001 (Court House) Noise Monitor - 5/5/25 to 6/13/25

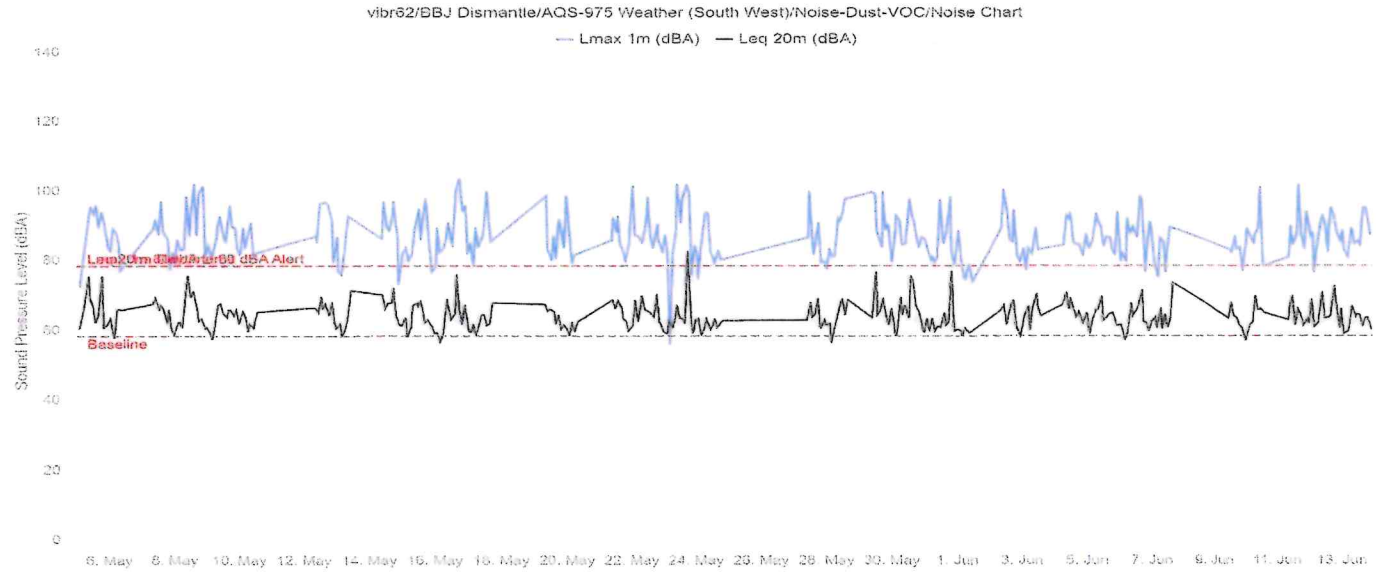


AQS-975 Weather (South West) Noise Monitor - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.


EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

2. Community Air Monitoring Weekly Data Summary: Noise Monitoring - 5/5/25 to 6/13/25

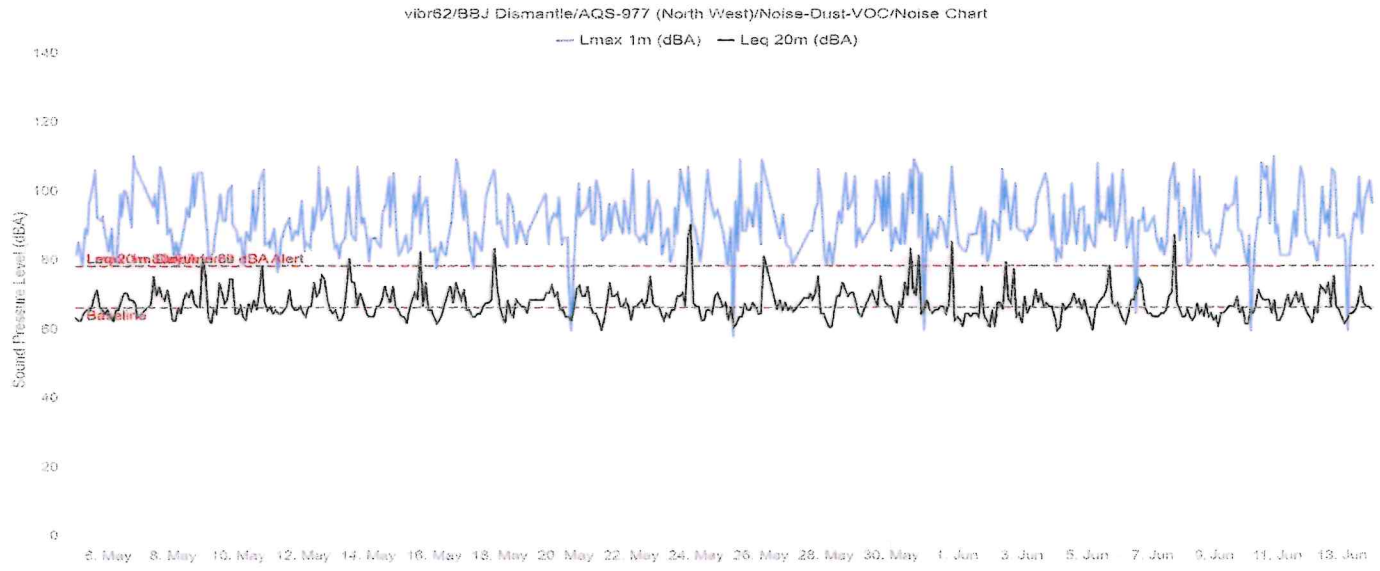

AQS-977 (North West) Noise Monitor - 5/5/25 to 6/13/25

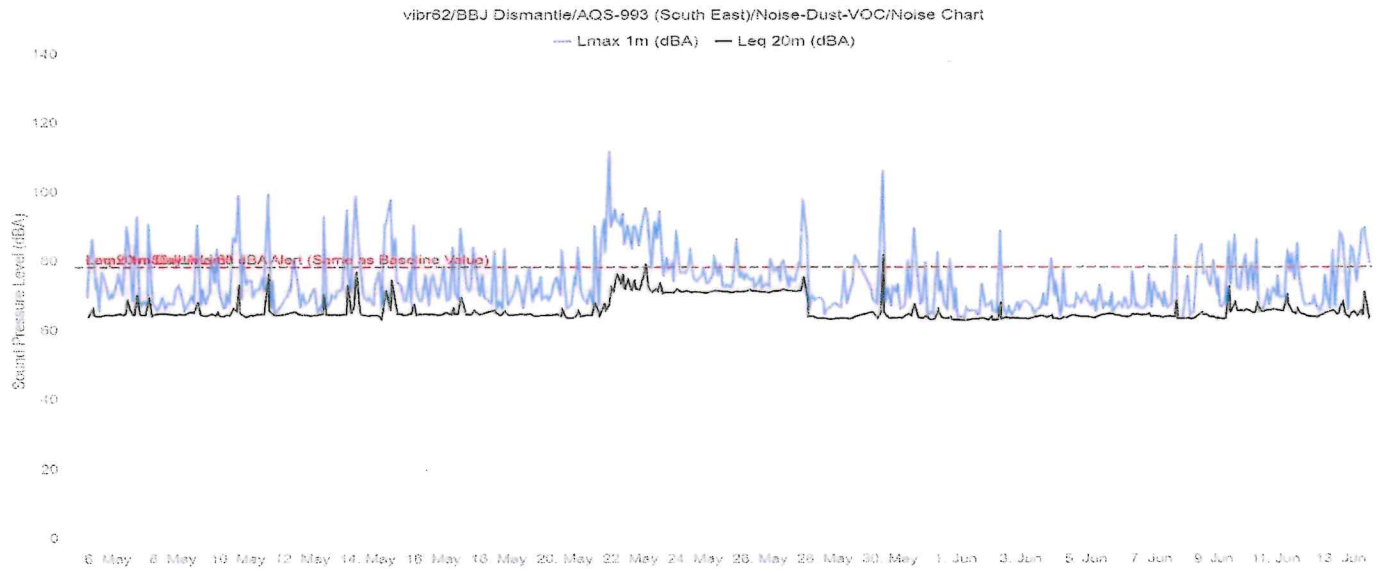


AQS-993 (South East) Noise Monitor - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.


EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

2. Community Air Monitoring Weekly Data Summary: Noise Monitoring - 5/5/25 to 6/13/25

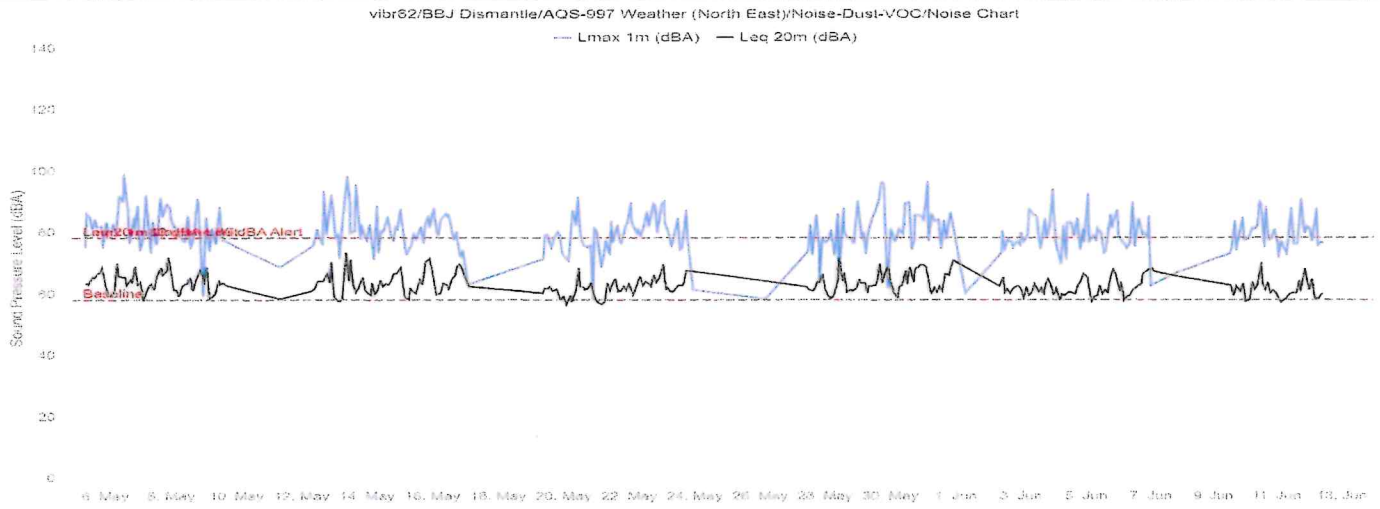

AQS-997 Weather (North East) Noise Monitor - 5/5/25 to 6/13/25

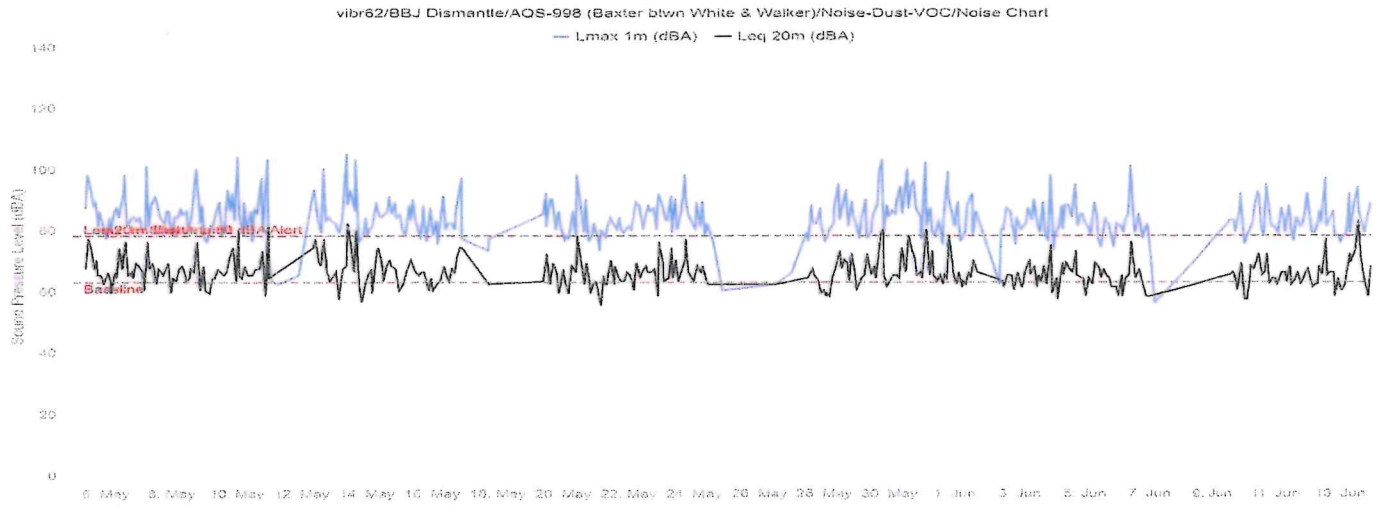


AQS-998 Baxter between White and Walker Noise Monitor - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.


EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

3. Community Vibration Monitoring Weekly Data Summary - 5/5/25 to 6/13/25

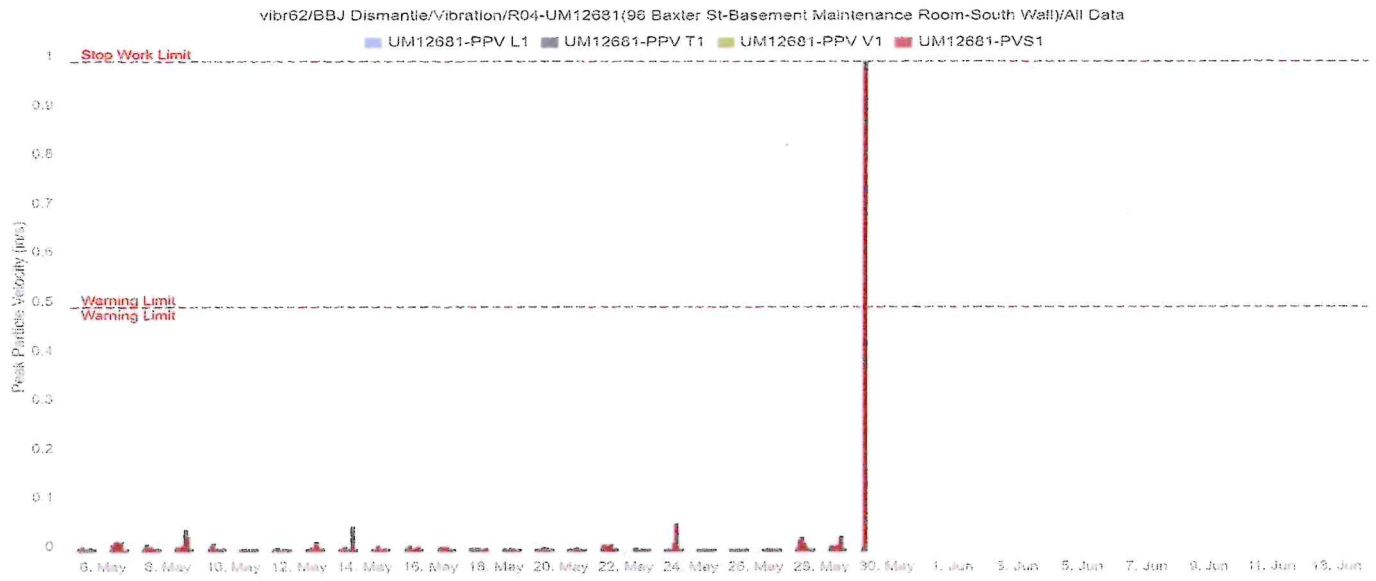

Vibration Monitor R04 -5/5/25 to 6/13/25

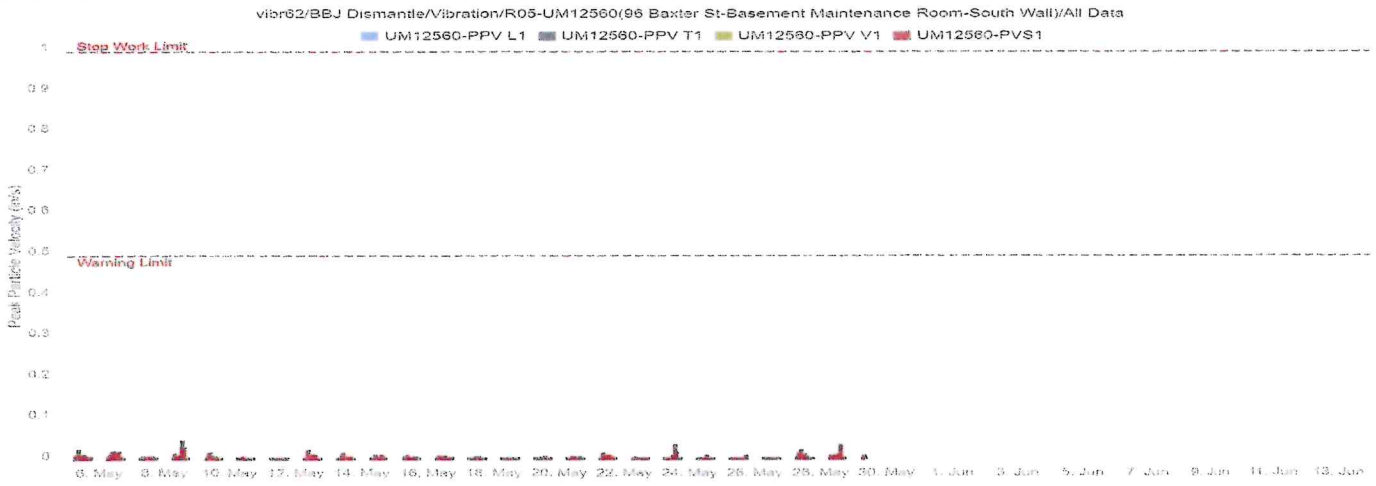


Vibration Monitor R05 - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.


EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

3. Community Vibration Monitoring Weekly Data Summary - 5/5/25 to 6/13/25

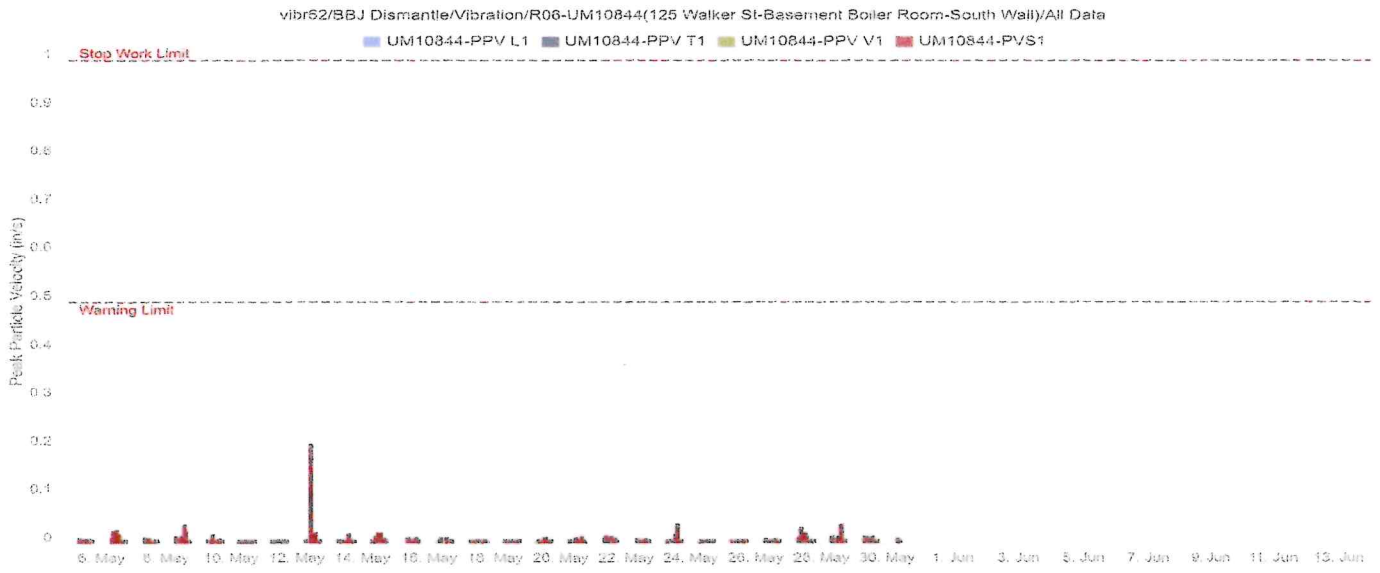


Vibration Monitor R06 - 5/5/25 to 6/13/25

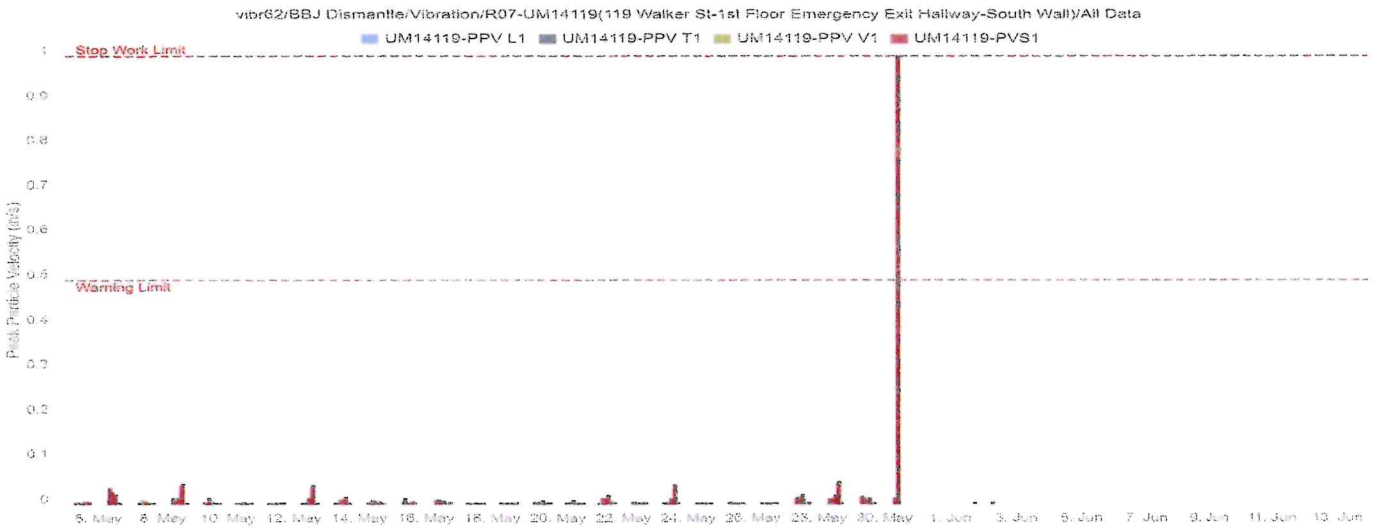


Vibration Monitor R07 - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.

3. Community Vibration Monitoring Weekly Data Summary - 5/5/25 to 6/13/25

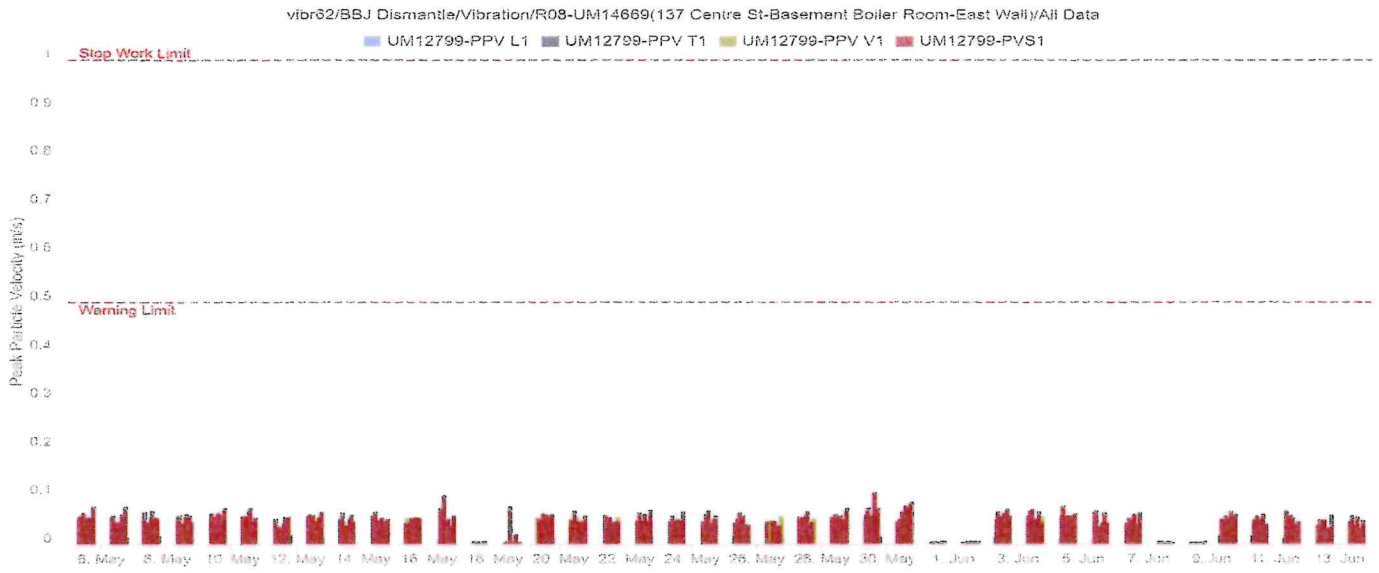


Vibration Monitor R08 - 5/5/25 to 6/13/25

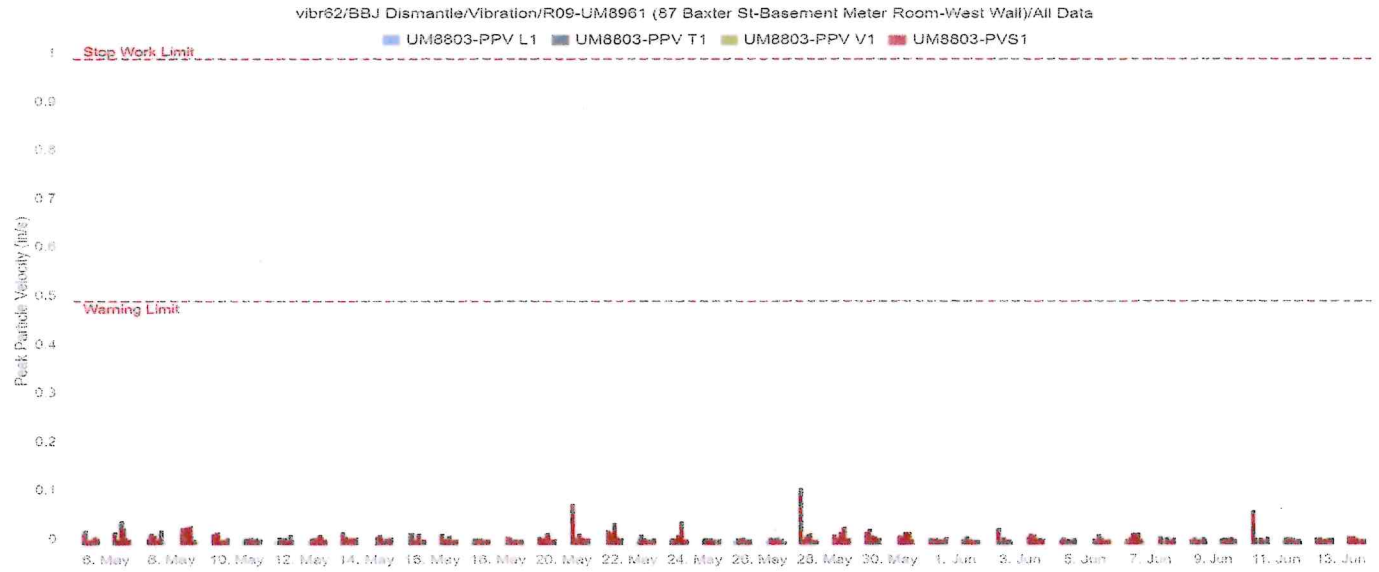


Vibration Monitor R09 - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.

3. Community Vibration Monitoring Weekly Data Summary - 5/5/25 to 6/13/25

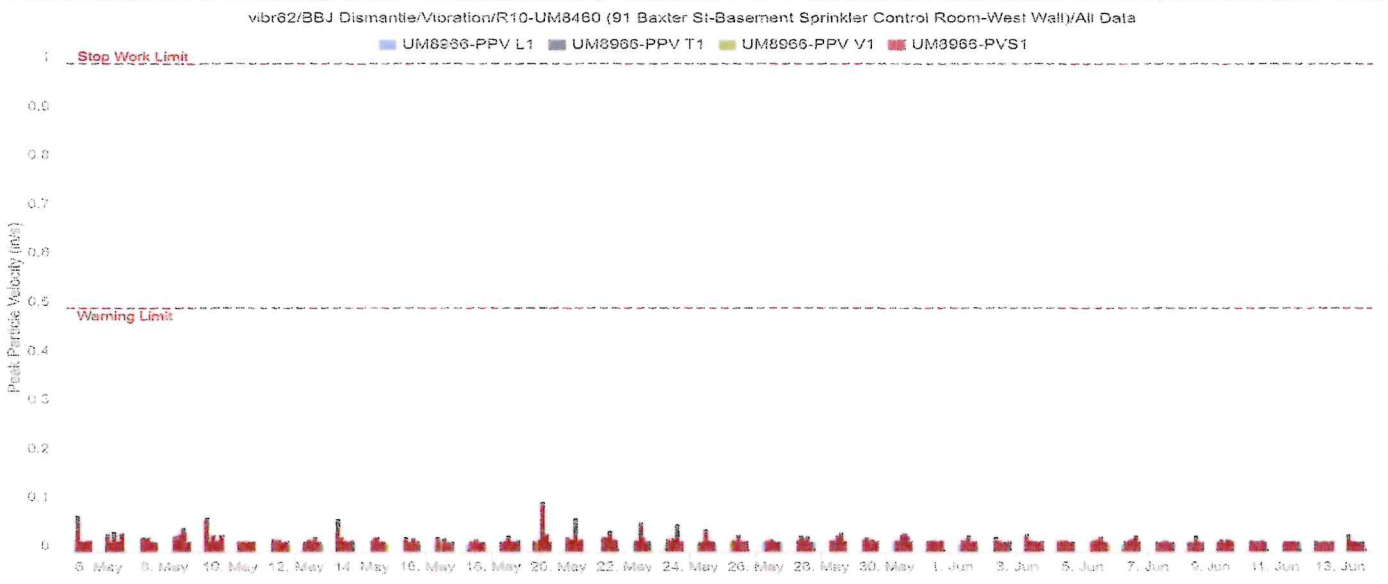


Vibration Monitor R10 - 5/5/25 to 6/13/25

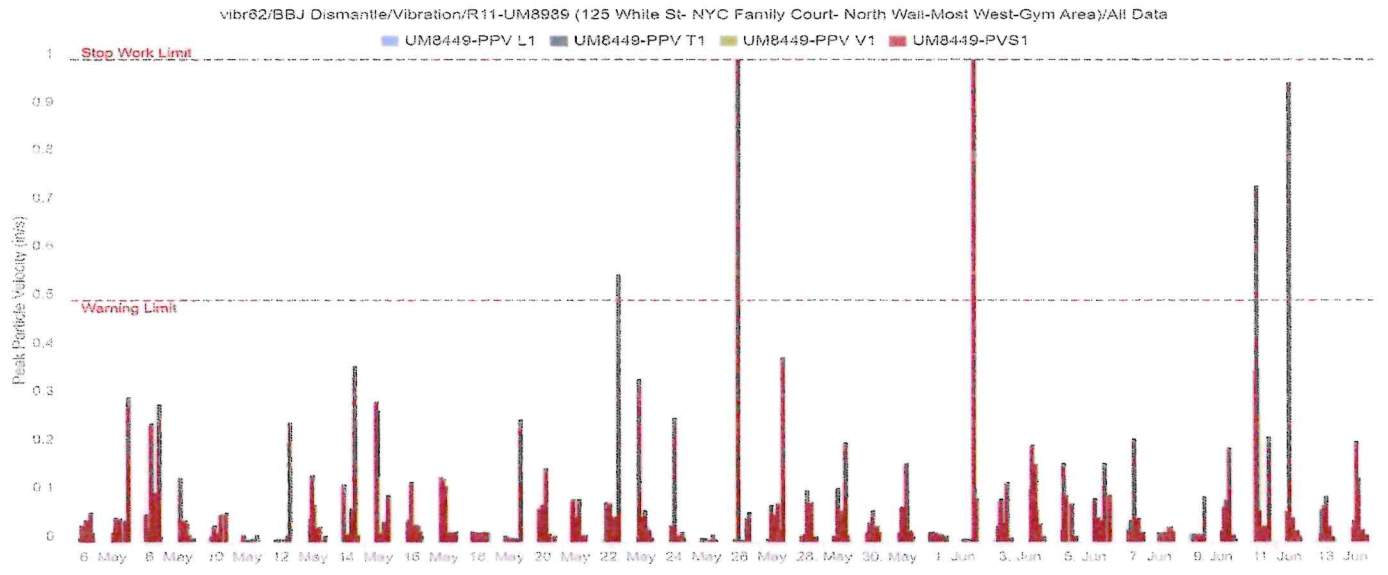


Vibration Monitor R11 - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.

3. Community Vibration Monitoring Weekly Data Summary - 5/5/25 to 6/13/25

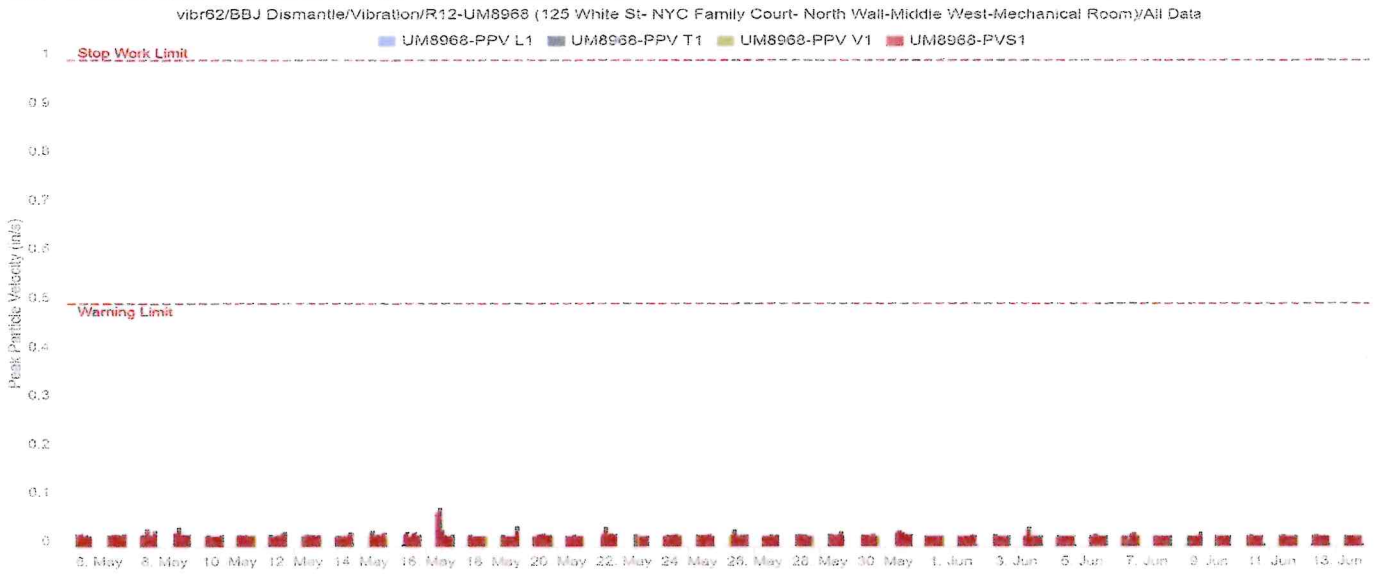

Vibration Monitor R12 - 5/5/25 to 6/13/25

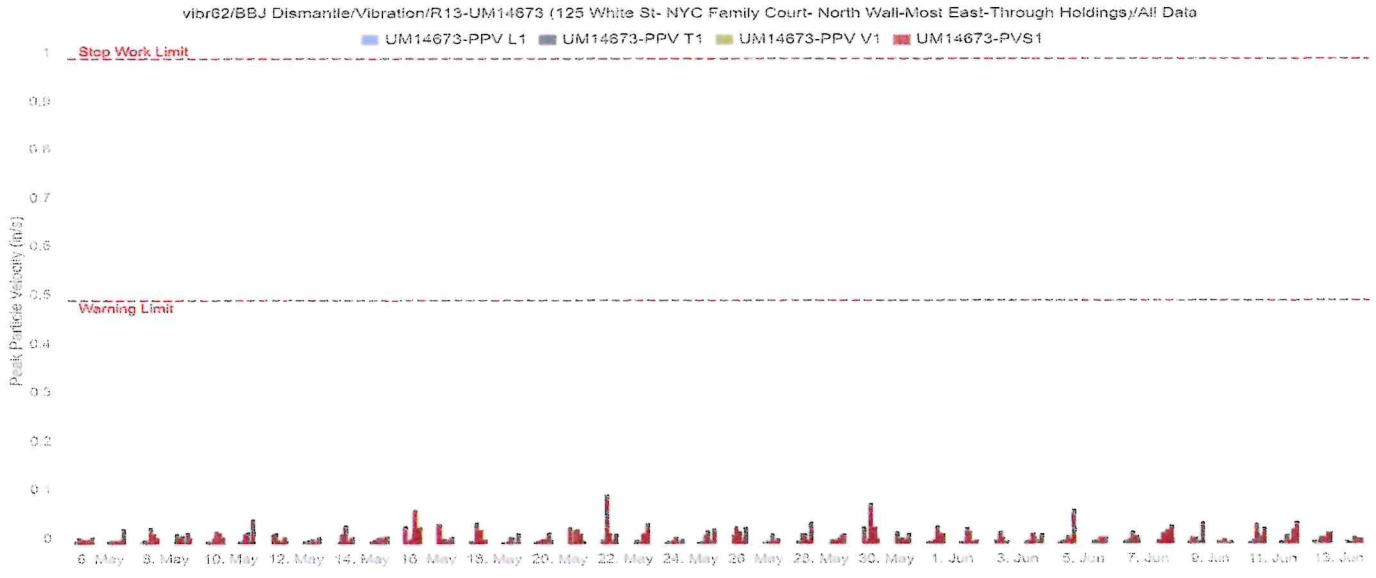


Vibration Monitor R13 - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.


EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

3. Community Vibration Monitoring Weekly Data Summary - 5/5/25 to 6/13/25

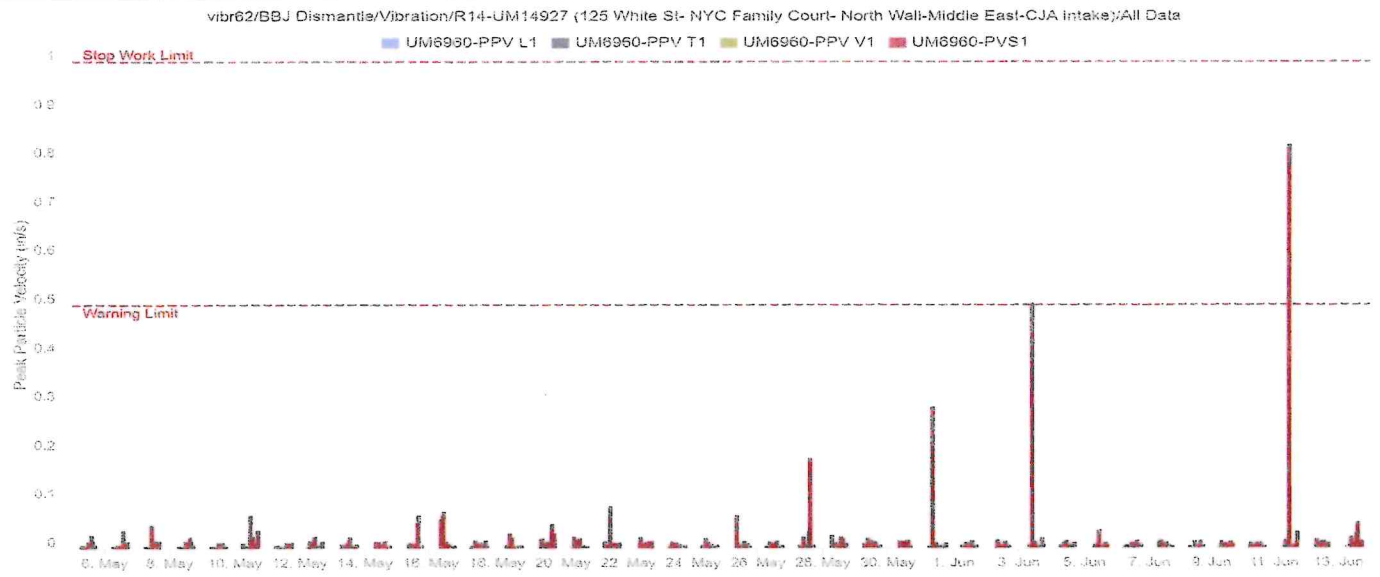

Vibration Monitor R14 - 5/5/25 to 6/13/25

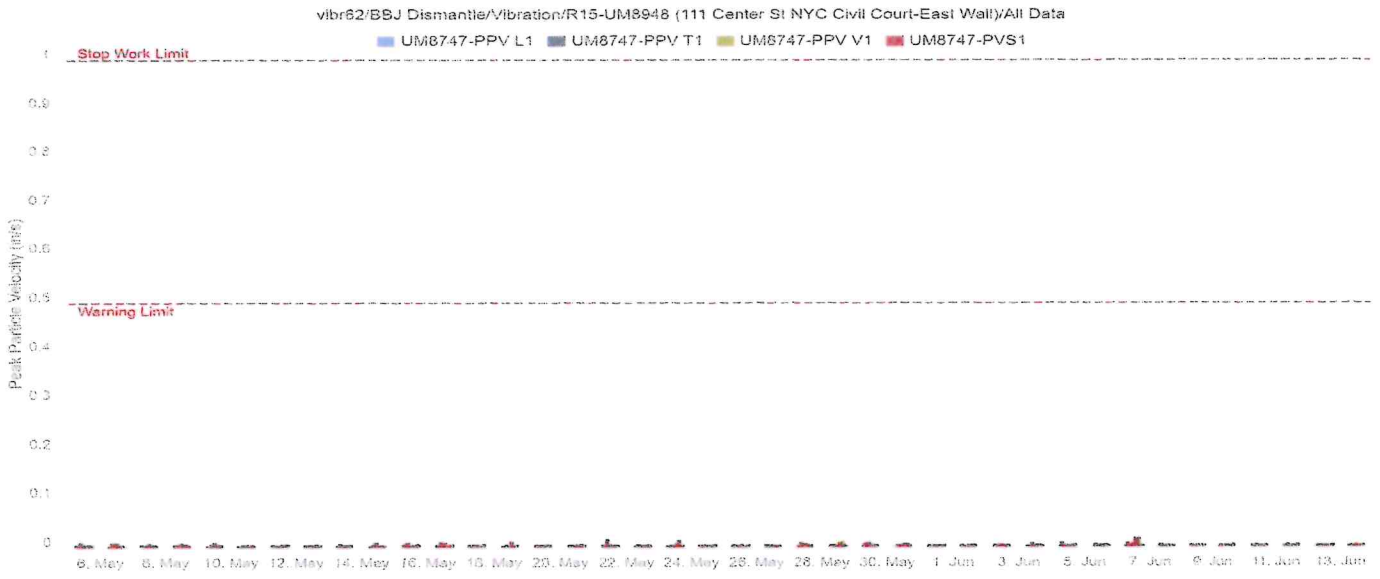


Vibration Monitor R15 - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.


EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

3. Community Vibration Monitoring Weekly Data Summary - 5/5/25 to 6/13/25

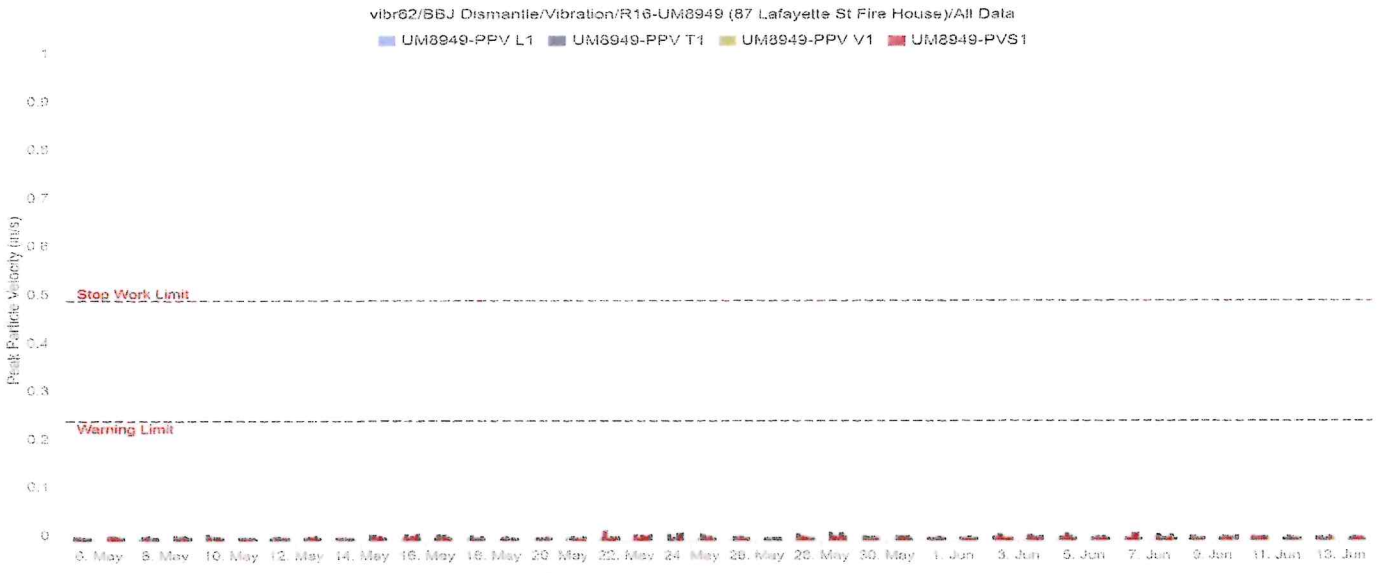

Vibration Monitor R16 - 5/5/25 to 6/13/25

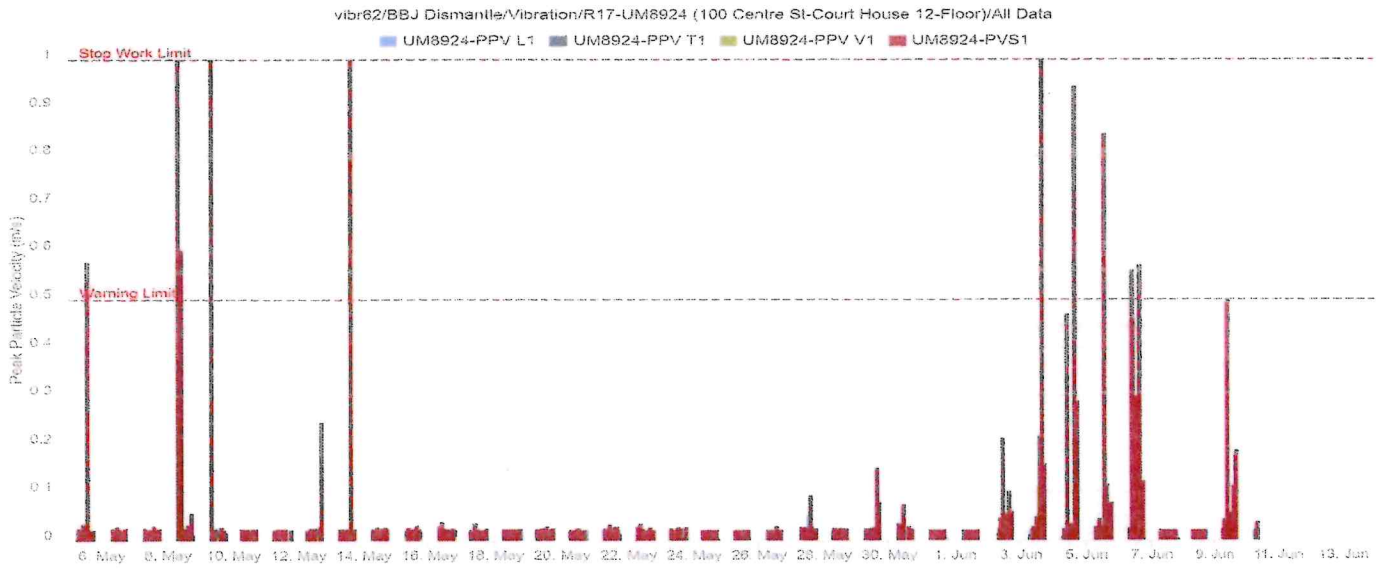

Vibration Monitor R17 - 5/5/25 to 6/13/25

Cc:	Lawra Dodge & Tim Novy	By:	Brian Ehalt & Megan DeMatteo
			Excel Environmental Resources, Inc.

EXCEL Environmental Resources, Inc.

WEEKLY INDEPENDENT COMMUNITY DATA SUMMARY REPORT No. 6

4. Photographic Summary: Photo 1: View of main gate entrance and sidewalk along Centre St. looking east towards the Site.



Photo 2: View of Centre and White Streets looking west from the Site entrance.



Photo 3: View of Center St. and the sidewalk looking Southwest from the Site entrance area.

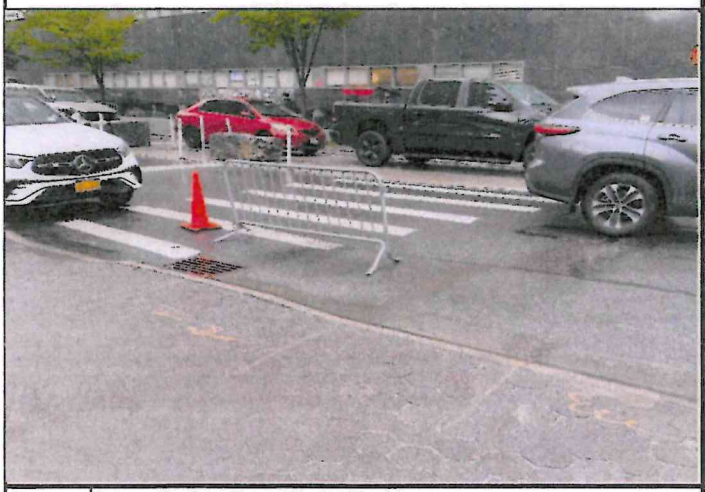


Photo 4: View of the sidewalk and Centre St. looking south towards the courthouse and CAMP station AQS-975.



Cc:	Lawra Dodge, Brian Ehalt, Tim Novy	By:	M. DeMatteo
			Excel Environmental Resources, Inc.

Photo 5: View from the Site looking west towards the main entrance gate to the east showing steel plates used to facilitate equipment	Photo 6: View of the courthouse looking south showing the 3rd and 12th floor infill work locations.
	
Photo 7: View of the courthouse lookine southeast showing the 3rd floor infill and corner of the building brick, or stone, work.	**Photo 8: View of the courthouse infill work in progress.**
	

Cc:	Lawra Dodge, Brian Ehalt, Tim Novy	By:	M. DeMatteo
			Excel Environmental Resources, Inc.

Photo 9: View of the courthouse brick, or stone, work in progress.	Photo 10: View of the courthouse brick, or stone, work in progress.
	
Photo 11: View of the interior of the Site facing northeast showing the wet ground surface conditions.	**Photo 12: View of a parked excavator and rolloff containers staged in the central section of the Site and wet ground conditions.**
	

Cc:	Lawra Dodge, Brian Ehalt, Tim Novy	By:	M. DeMatteo **Excel Environmental Resources, Inc.**

Photo 13: Closer view of a parked excavator and rolloff containers staged in the central section of the Site and wet ground conditions.



Photo 14: View of the Chung Pak bldg. facing northwest showing the graded crushed concrete in the former North Tower basement area.



Photo 15: Closer view of the Chung Pak bldg. facing northwest showing the graded crushed concrete in the former North Tower basement area.



Photo 16: Close-up view of the Chung Pak bldg. facing northwest showing the graded crushed concrete in the former North Tower basement area.



Cc:	Lawra Dodge, Brian Ehalt, Tim Novy	By:	M. DeMatteo **Excel Environmental Resources, Inc.**
